



WMC AMERICAN UNIVERSITY EAST CAMPUS
SITE PLAN RENDERING
05.13.2014

L01

American University East Campus Community Meeting February 11, 2016


Agenda

- I. Project Status Update
- II. 6-Month Look Ahead
- III. Pre-cast Facade Delivery and Installation
- IV. Q & A

Status update

- Garage and Building 2 and 3 structures completed
- Pre-cast façade elements completed, delivery to start within two weeks, and installation to commence immediately after
- Interior fit-out has commenced in garage and Building 2 and 3
- Building 1 structure to be completed by end of February followed by Buildings 4 and 6 (Buffer) in March
- Target completion/occupancy for Buildings 2 and 3 August 2016, October 2016 for Building 1, 4 and 6 (Buffer) buildings

Status update

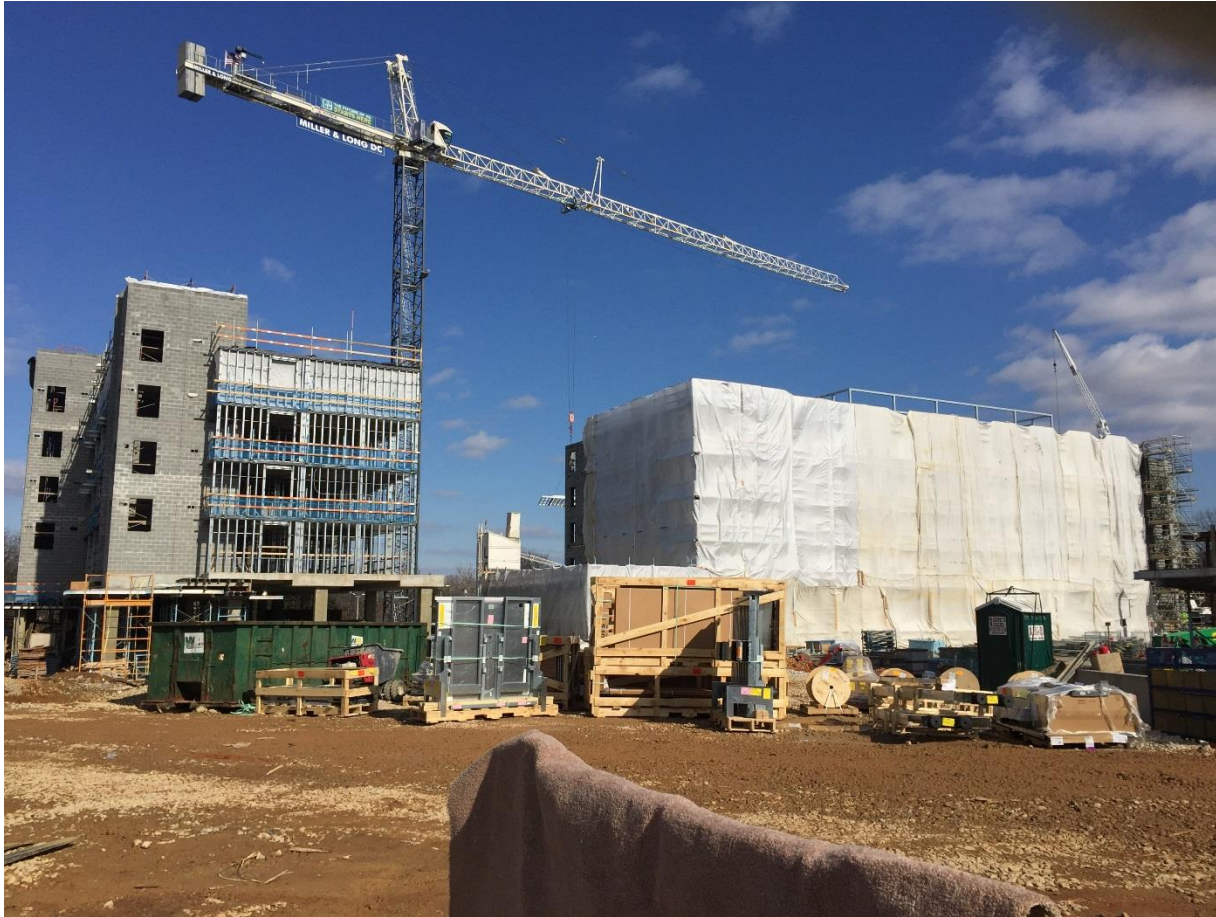

Buildings 1 and 3

Status update



Courtyard view from Building 3


Look Ahead

East Campus Project

Six Month Look-Ahead Schedule

2016						
Phase	February	March	April	May	June	July
Above grade structure	█					
Pre-cast Installation		█				
Interior Fit-out	█					
Sitework		█				

Look Ahead – Pre-cast Facade

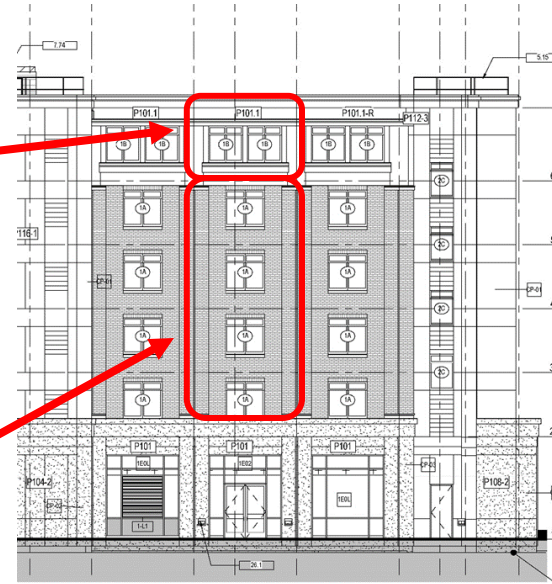

Pre-cast Delivery and Installation

- Oversized vehicles escorted from DC/MD border at Connecticut Avenue to site
- 3 - 4 trucks at a time, 12-14 per day Monday – Thursday
- Between the hours of 10:30am and 2:00pm
- Materials will be stored on site until installed
- Mobile crane used to install panels
- DDOT traffic advisory will be issued

Skanska Onsite Team



David Coleman
Project Executive



Elias Bezabhe
Project Manager



Steve Griffin
Assistant Superintendent



Eric Henson
Superintendent

301-704-9176
AUEC@skanska.com

American University Team

Andrew Huff

Director of Community Relations

202.440.2221

ahuff@american.edu

Robert van Hoek

Senior Project Manager

202.885.1142

vanhoek@american.edu

Onyel Bhola

Project Coordinator

240.565.7707

onyel@american.edu

**American University
Public Safety
202-885-2527**

Q & A

